

Northwest Regional Water District has never used Lead service lines. Northwest Regional Water District began in the early 1970's and only purchased 1" p.e. service line. We have purchase records showing the purchase of 1 inch p.e. pipe.

Most of our sampling sites were built before 1998 and many of those are Tier I sites. Many of the homes on our system have had their internal plumbing changed to plastic. We focused on sampling on homes built in the few small villages in our area with older homes containing copper plumbing.

We have included several maps of our sampling locations

Public Side, Homeowner Side

- SMP Id's (LC ####)



Non-lead, Low Risk



Non-lead, Med Risk



Non-lead, Lead



Non-lead, Non-lead



The gray shaded areas are LC #### sample sites that are considered low risk since the age of the structures served (built before 1982) and the possibility that they could contain some plumbing / or fixtures that were installed prior to the 1982 and or 1998 lead by weight regulations.



The purple shaded areas are LC #### sample sites that are considered a med risk due to the age of the home (Built in early 1900's) and the possibility that they could contain some plumbing / or fixtures that were installed prior to the 1982 and or 1998 lead by weight regulations.



Areas marked solid green contain no lead service lines but contain copper plumbing which was installed after 1983

Northwest Regional Water District

PWS ID: OH7300003

123 Smith St. PO Box 158 McDermott, Oh 45652

M-F 8 am-4 pm

740-259-2789

800-993-9170

www.NWRWater.com

www.facebook.com/nwwater

Public Side, Homeowner Side


- SMP Id's


 Non-lead, Low Risk


 Non-lead, Med Risk


 Non-lead, Lead


 Non-lead, Non-lead

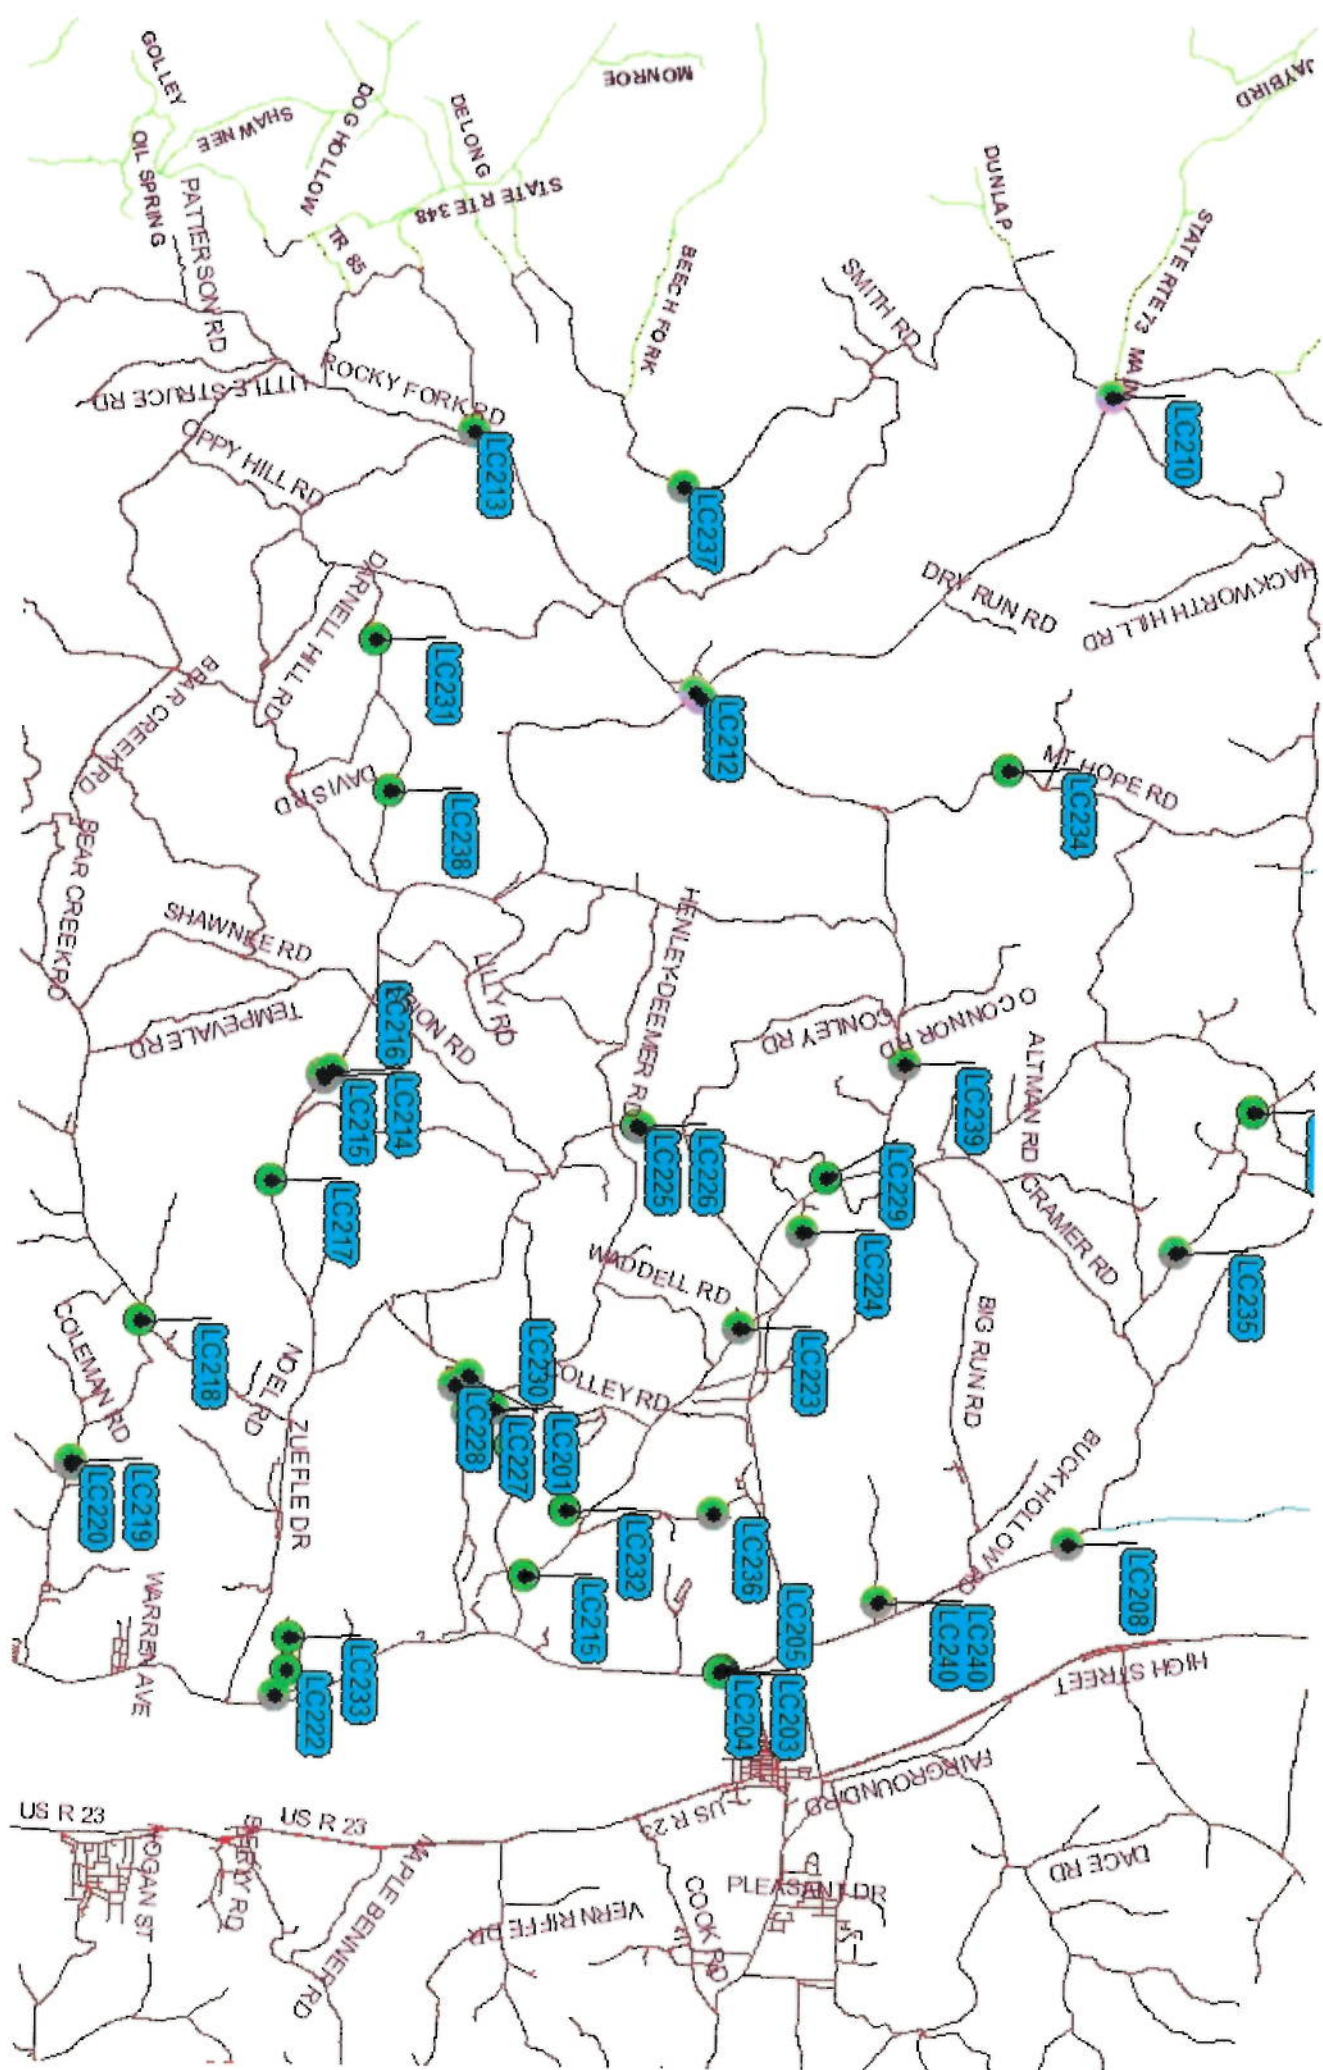


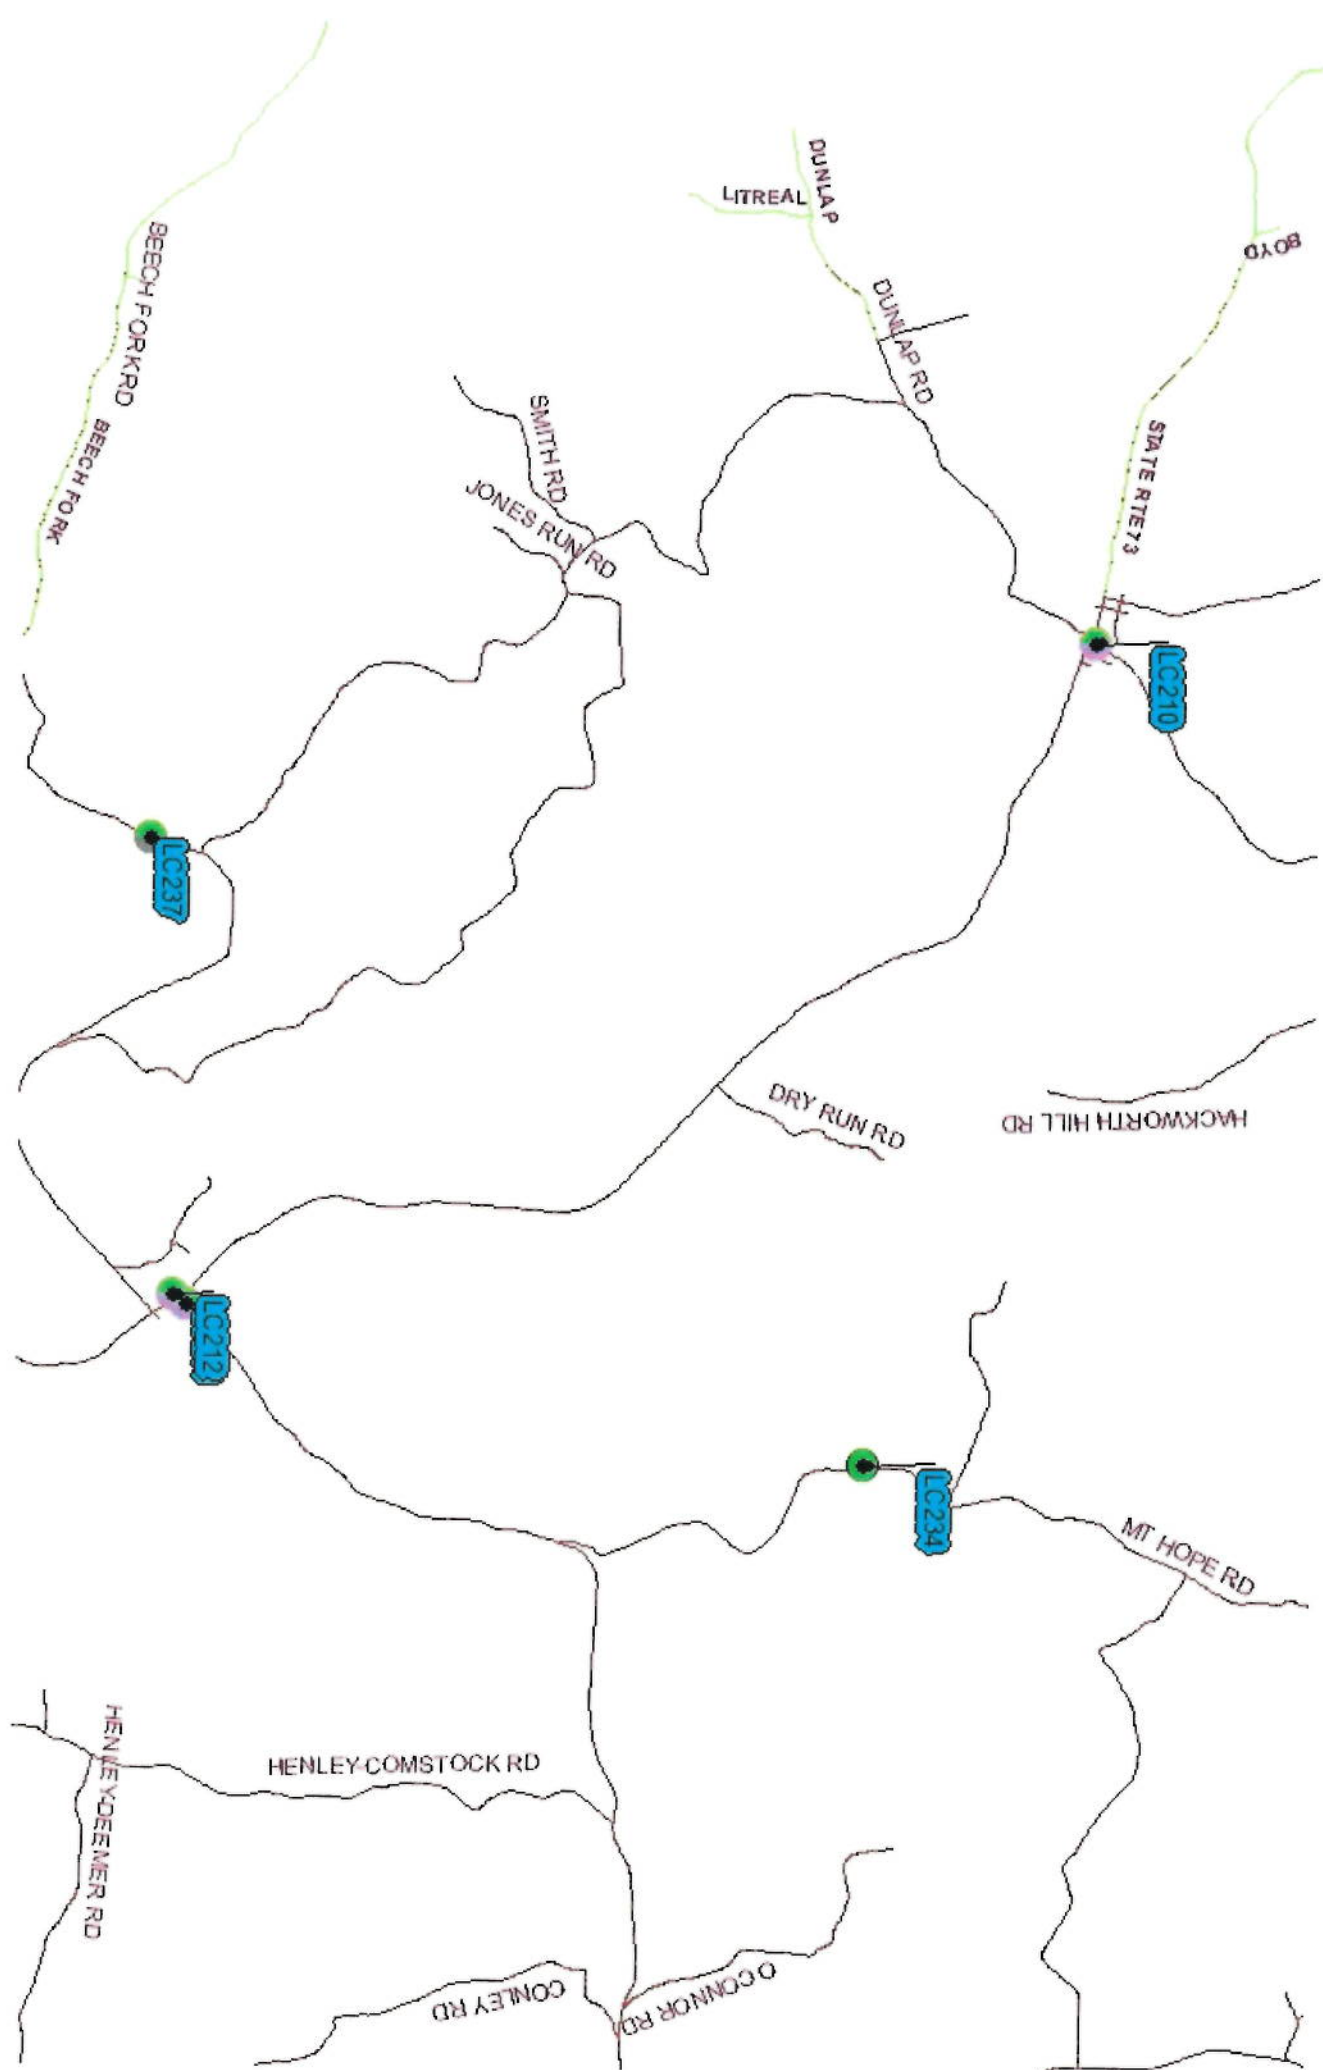

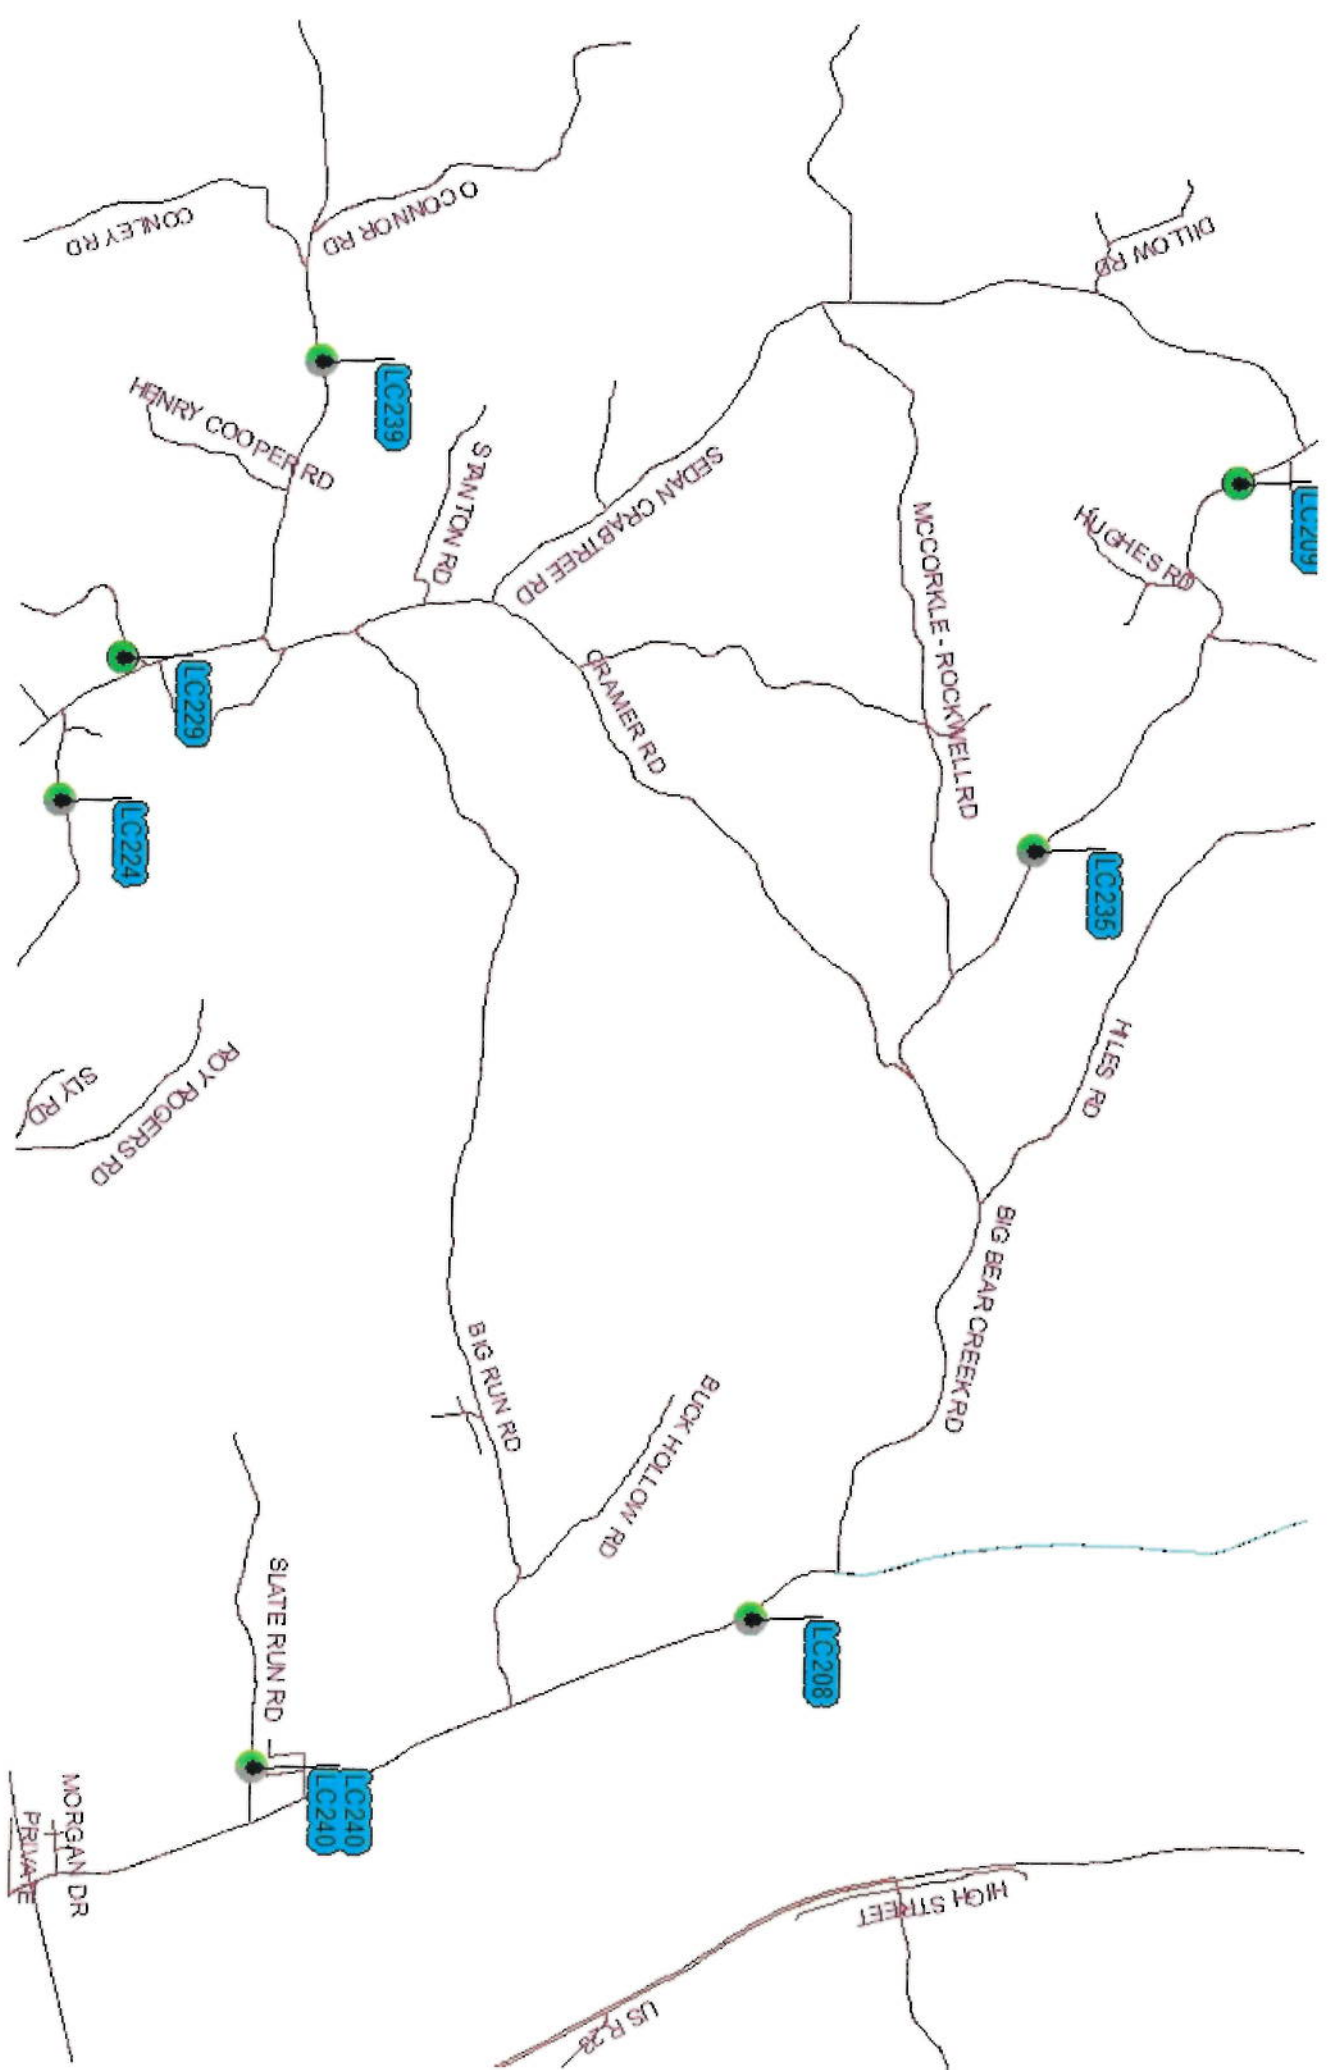


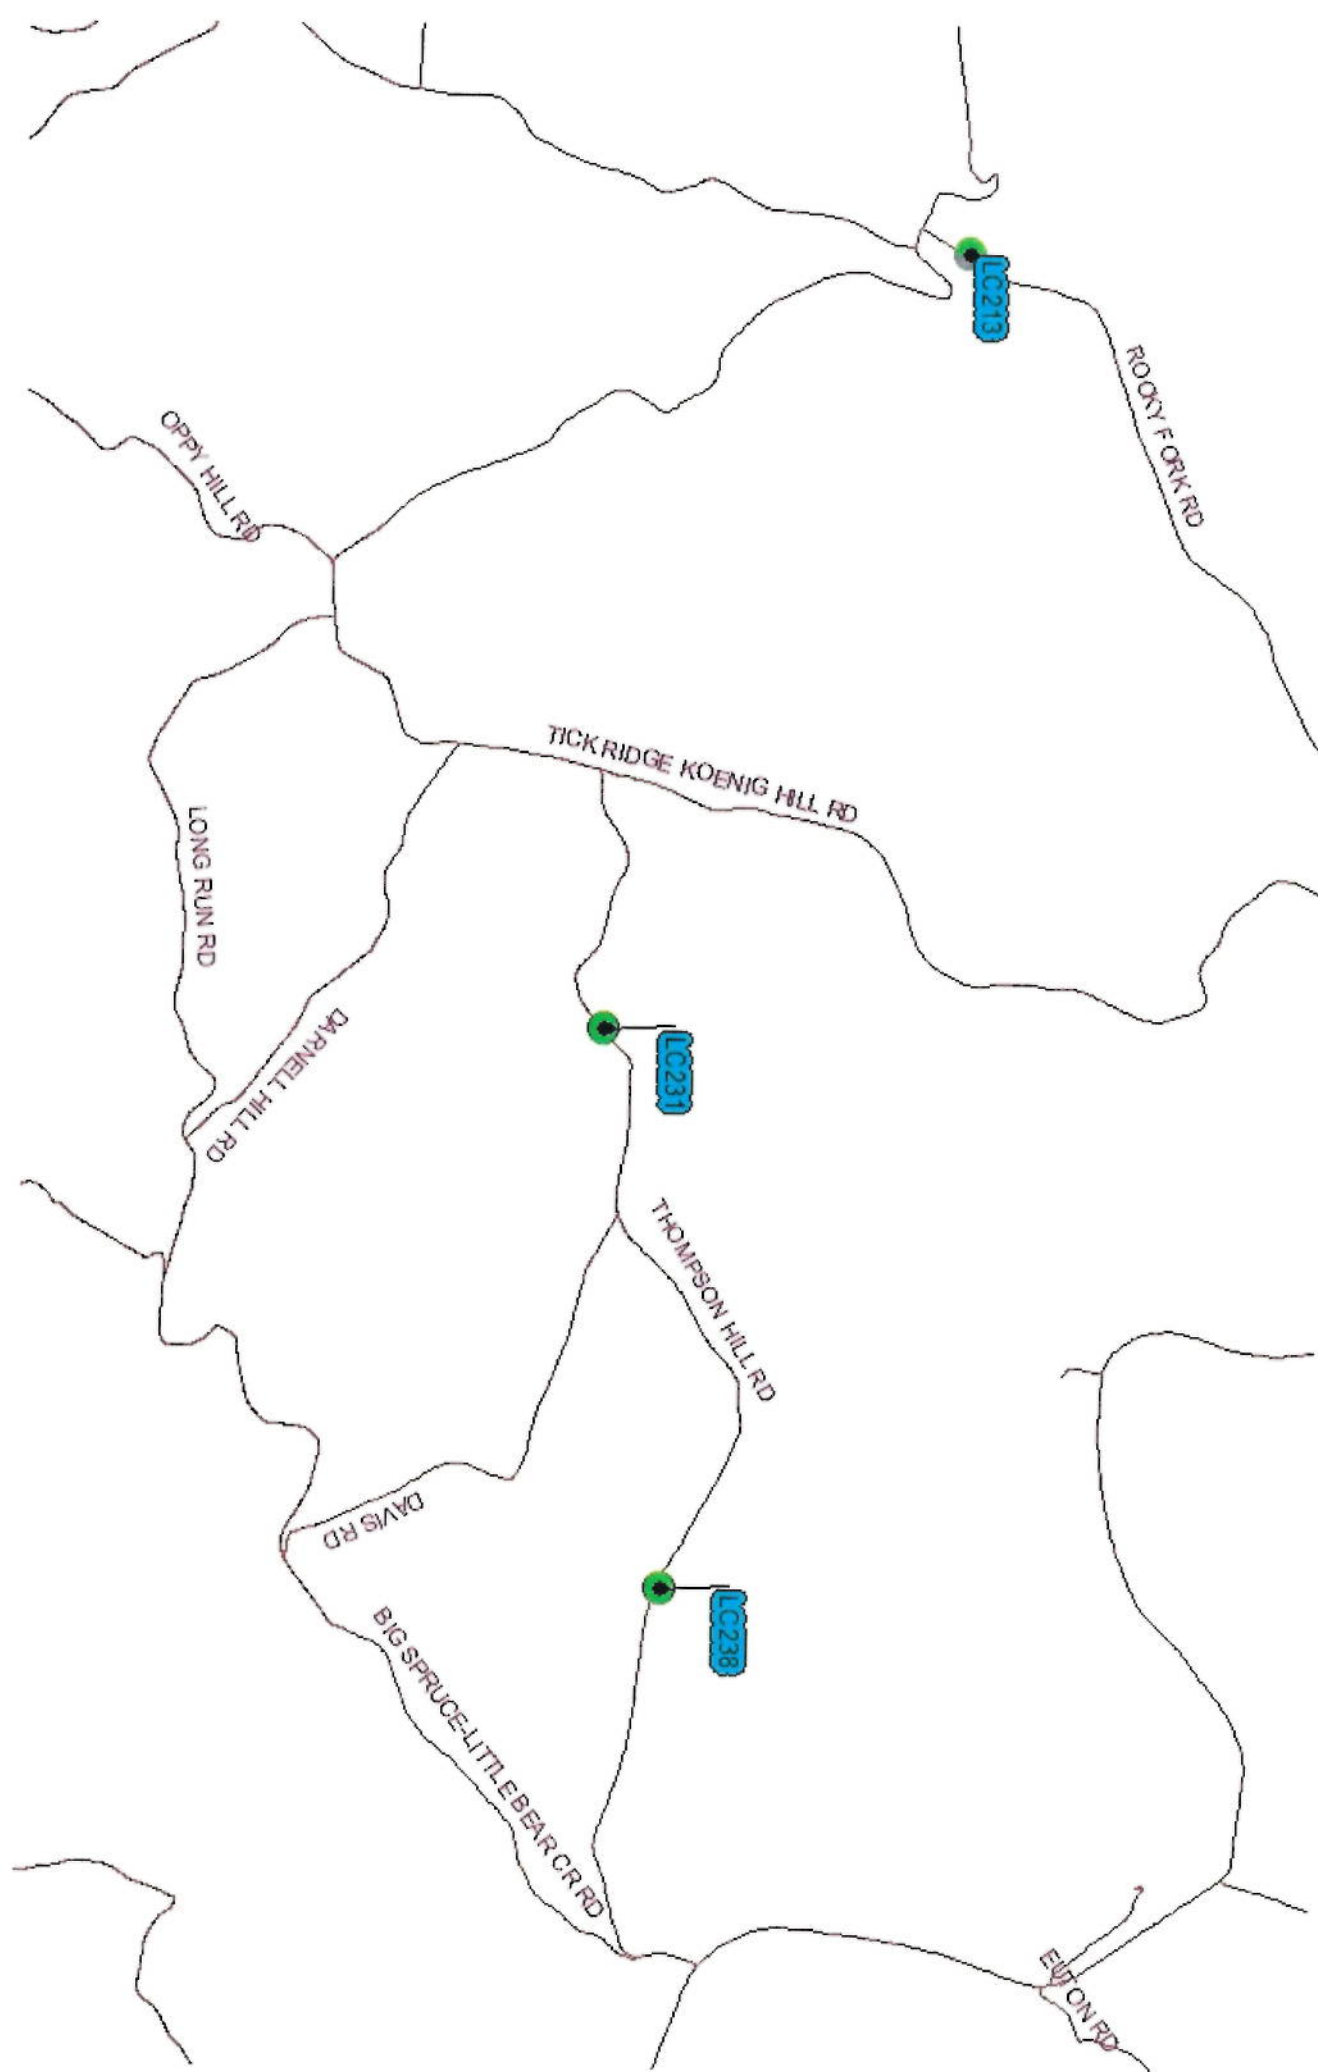

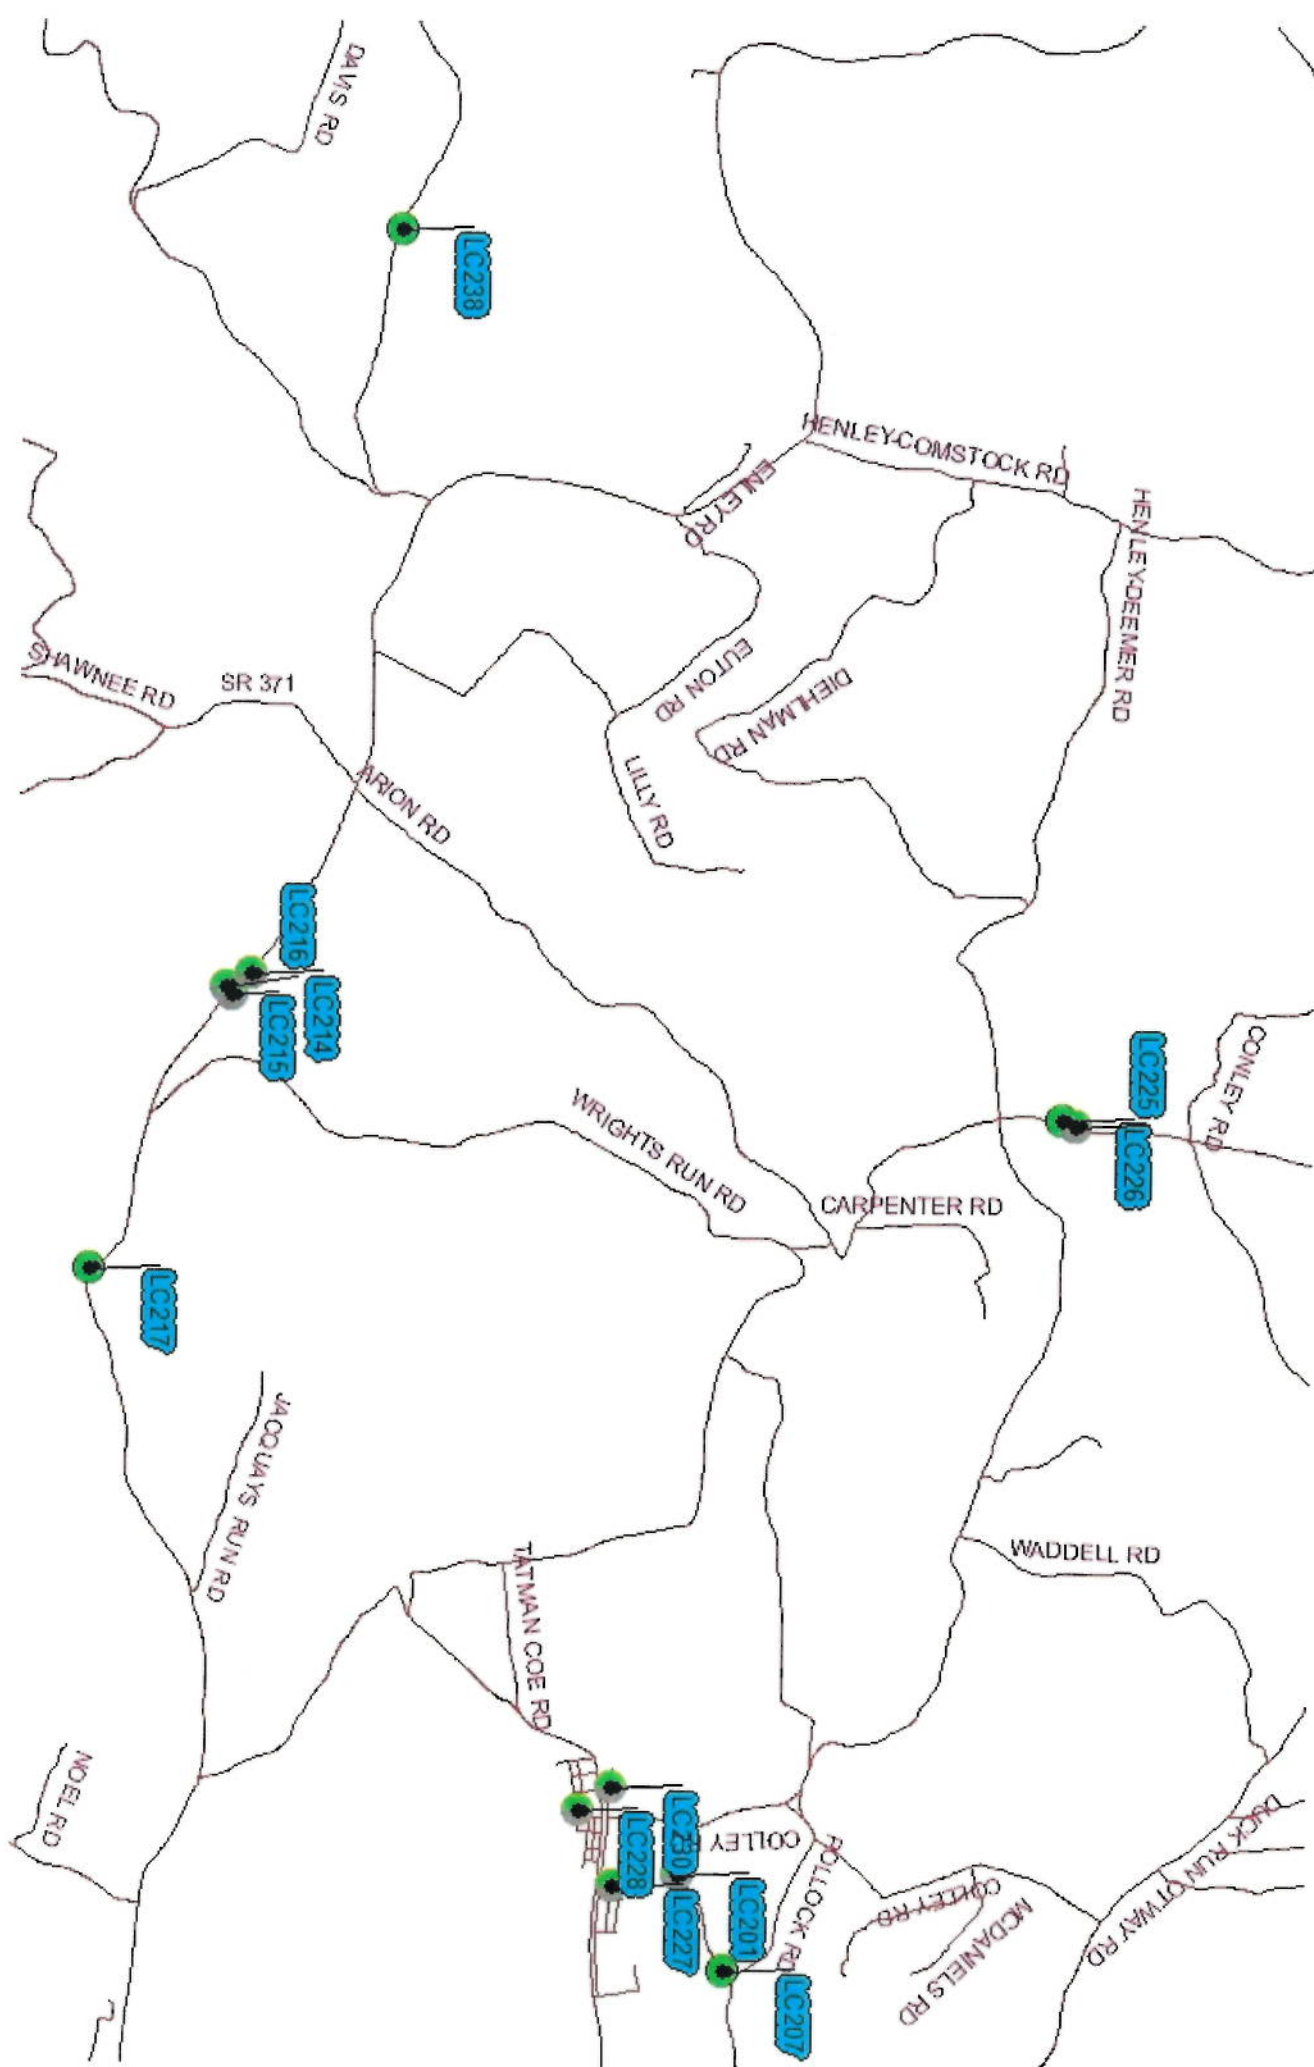

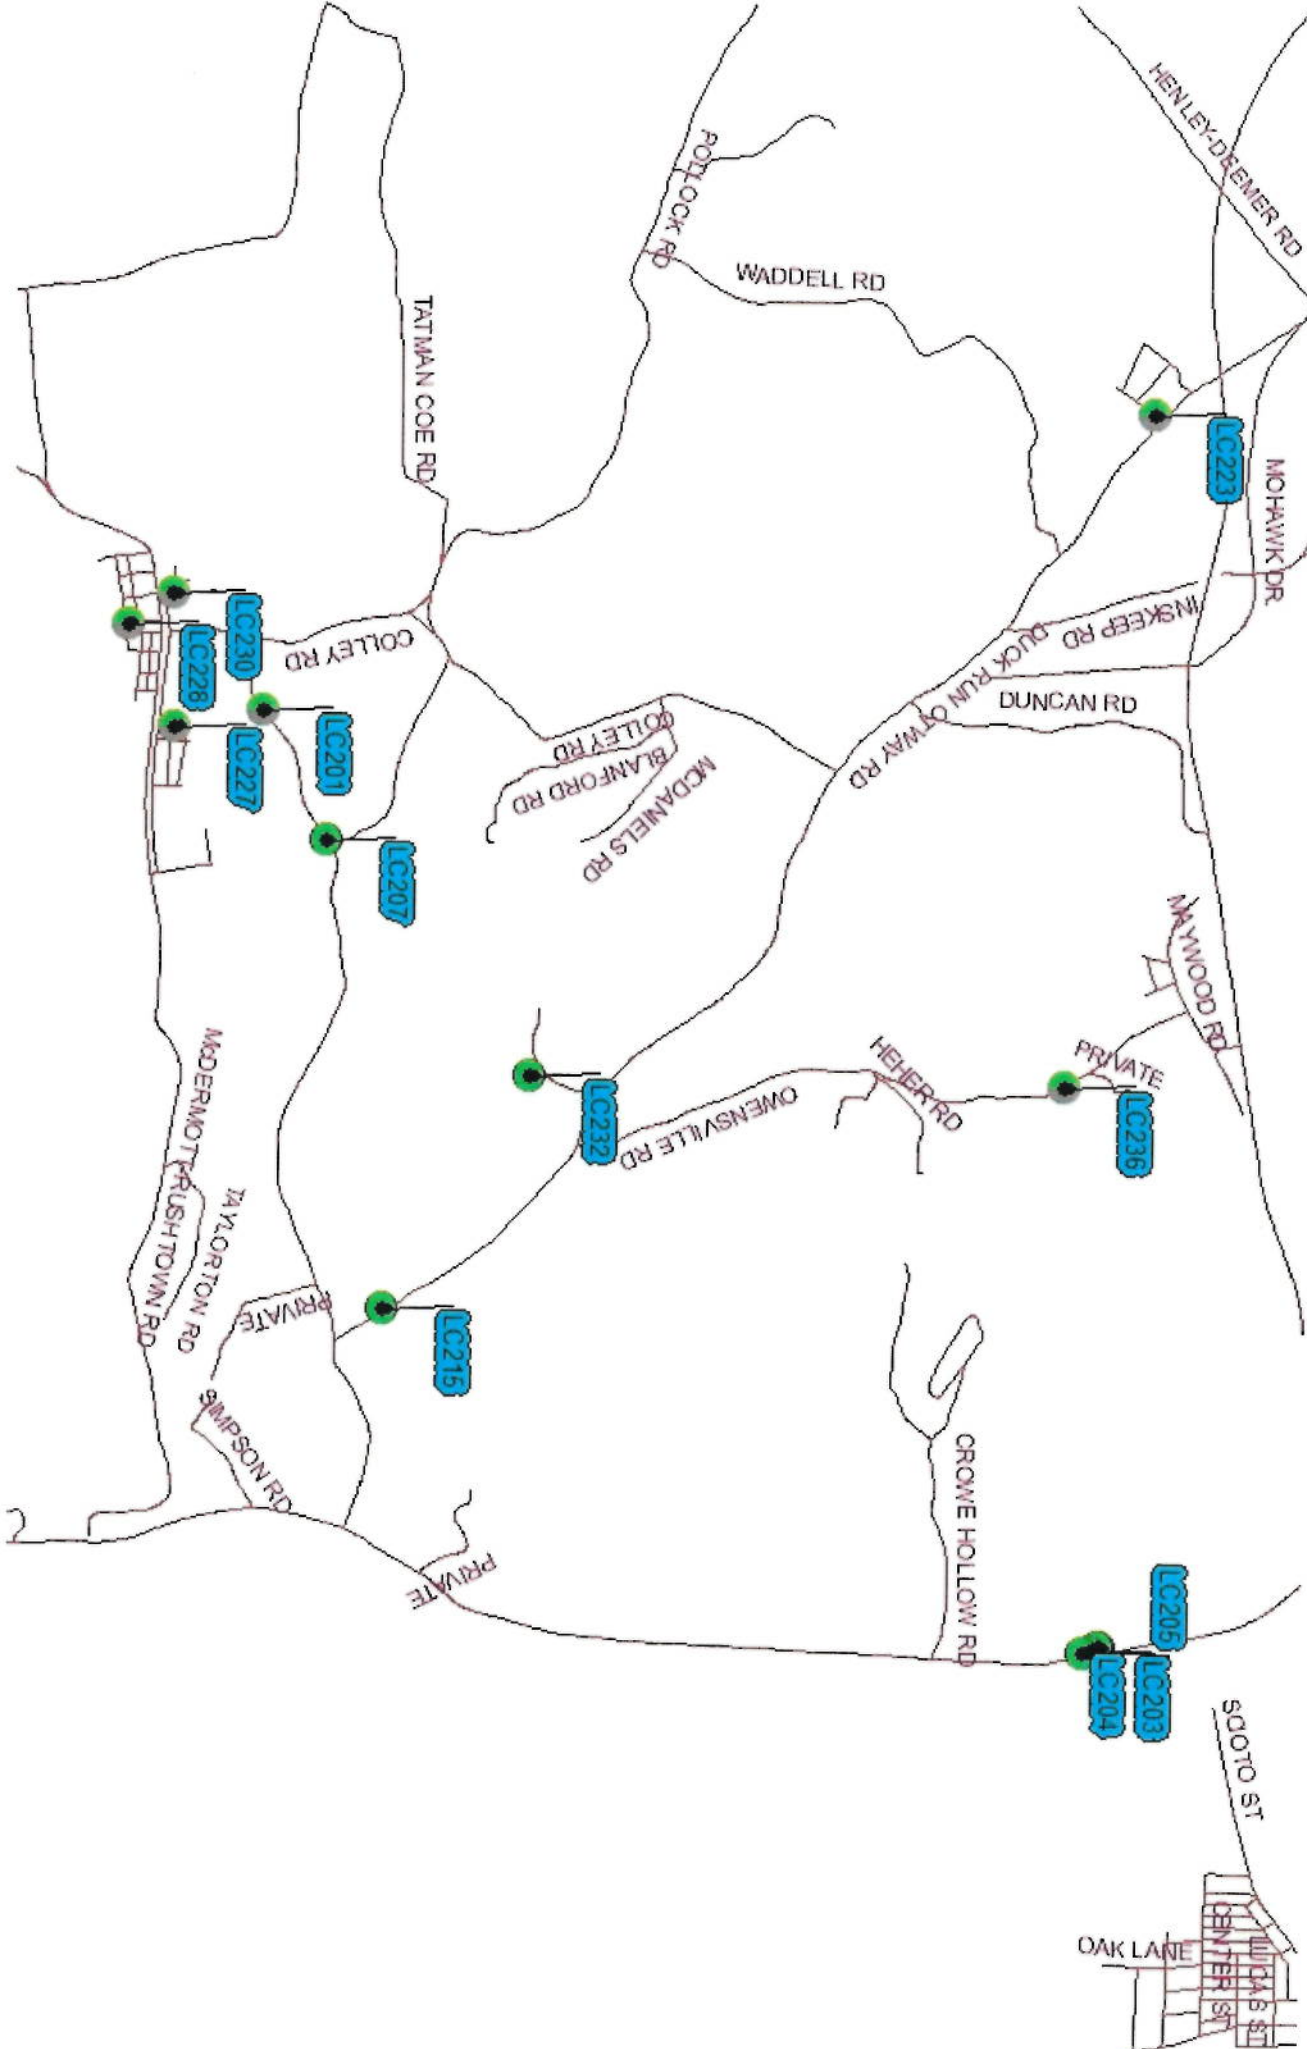



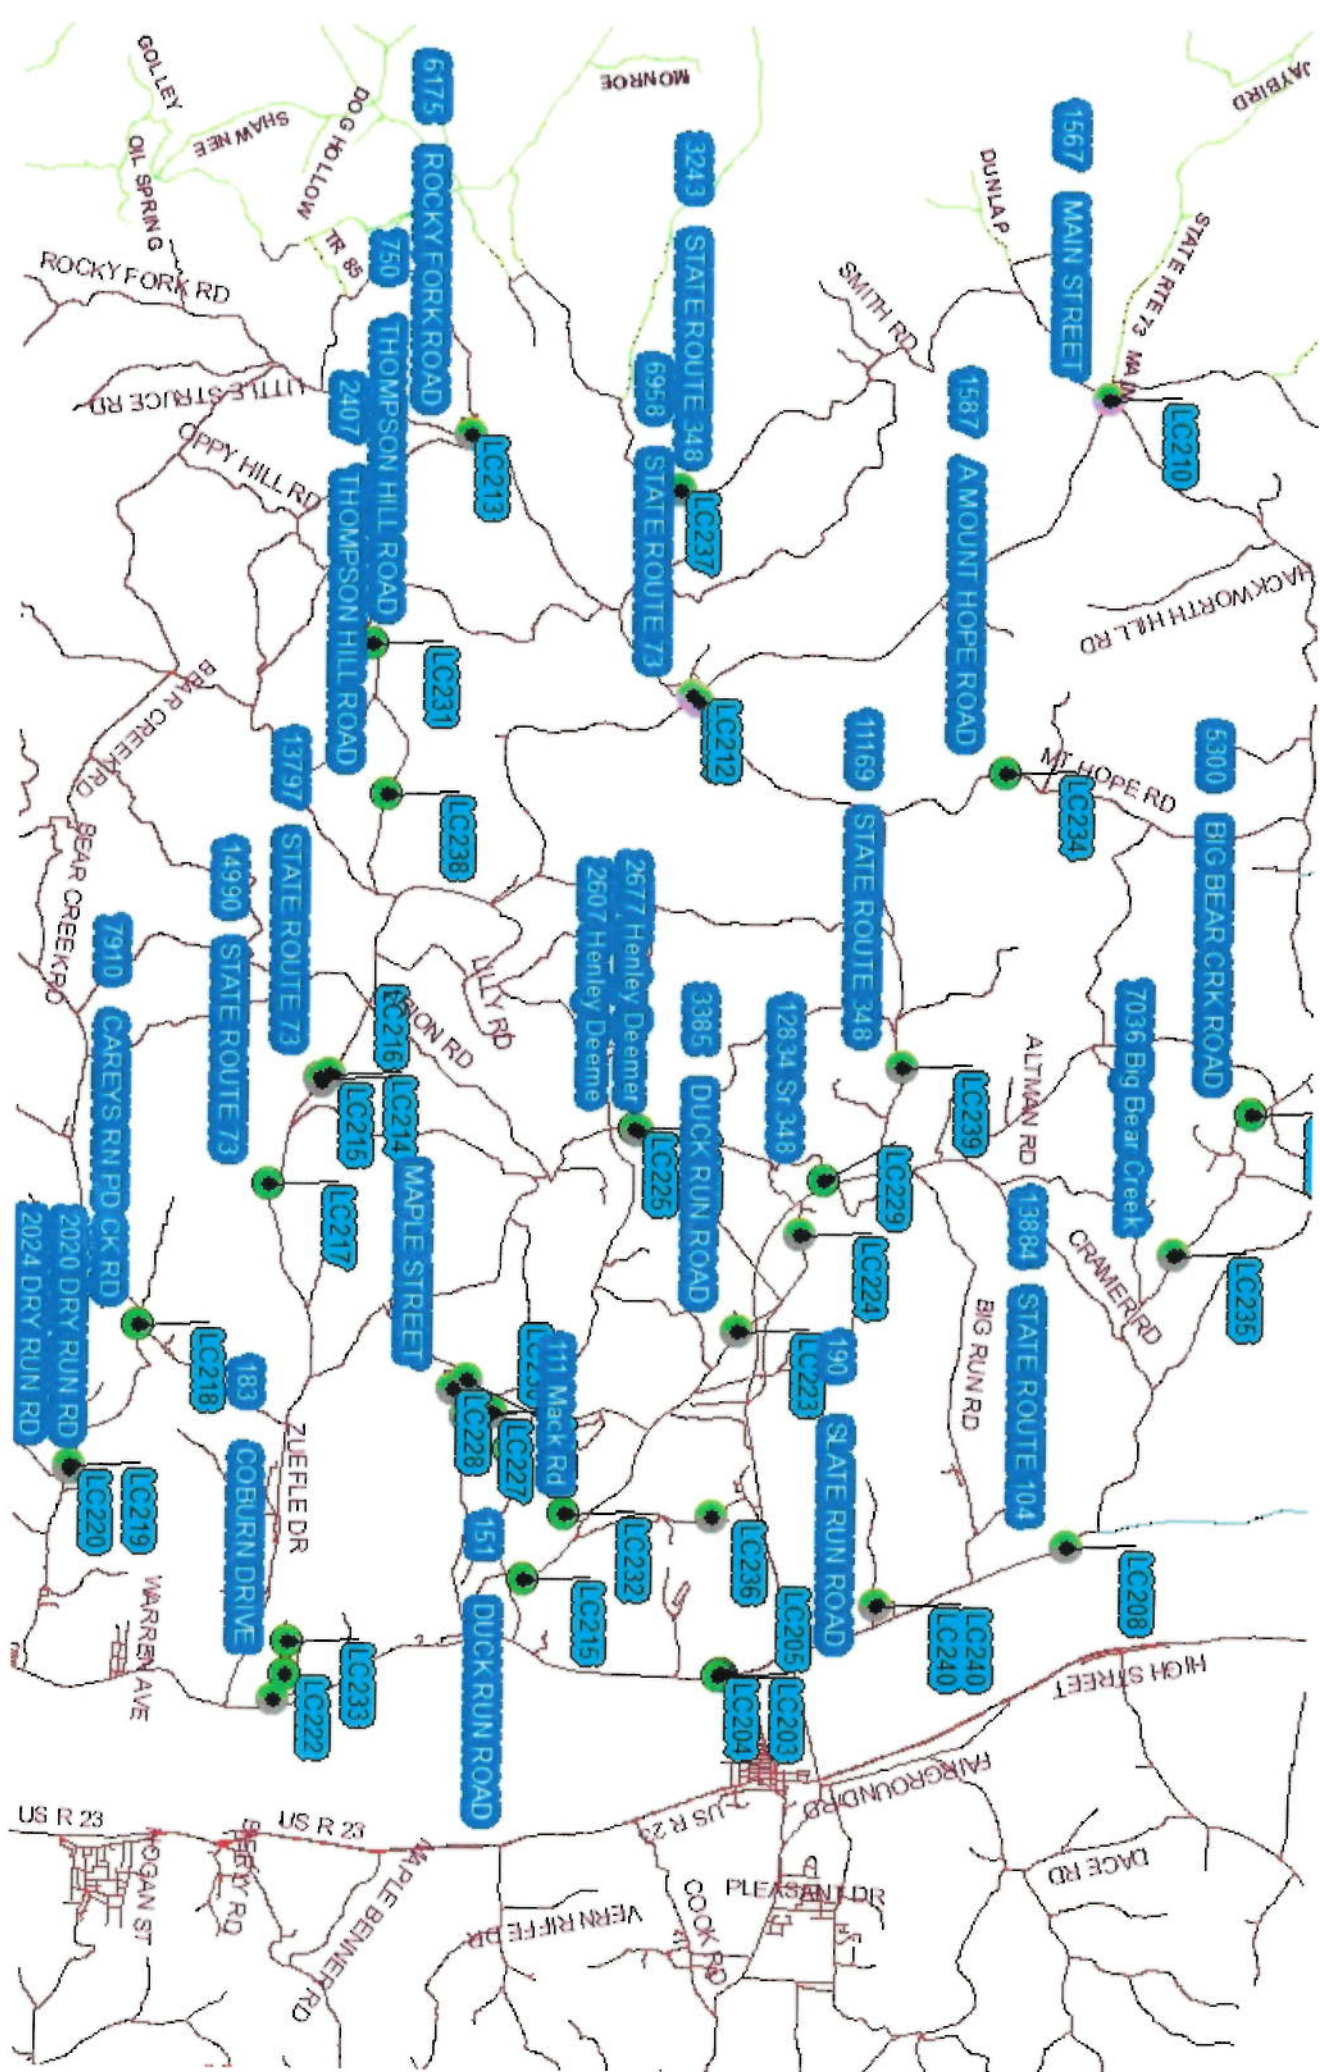

WATER WORKS & INDUSTRIAL SUPPLY CO.

TWX LISTINGS:
Water Wks Htg
 710-431-8009
Water Works Lex
 510-479-8811

OFFICE AND WAREHOUSE - 2525 GUYAN AVENUE
 P. O. BOX 885 TELEPHONE AREA: 304-525-7888
 HUNTINGTON, WEST VIRGINIA 25710

BRANCH OFFICES & WAREHOUSES
 LEXINGTON, KENTUCKY
 806-255-5335

TO: **Cox Const. Co.**

1815 Galena Pike

W. Portsmouth, Ohio

Date **November 8, 1972**

 Project **Northwest Water**

Systems INQUIRY

Gentlemen:
 We wish to submit our QUOTATION on the following list of material, delivery being

Please reference this quotation
 number when corresponding on
 items shown below.

Shipping Point

F. O. B. _____

Quotation # _____

72-141

MAKE OR ITEM	QUAN-TITY	SIZE	CATALOG NO.	DESCRIPTION	UNIT PRICE
1		2"x1"AWWA		McDonald Service Saddle for pvc pipe w/1" awwa tap	ea. 4.66
2		2 1/2"x1"AWWA		Ditto	ea. 5.40
3		3"x1"AWWA		Ditto	ea. 6.01
4		4"x1"AWWA		Ditto	ea. 6.25
5		5"x1"AWWA		Vega Ditto	ea. 7.30
6		6"x1"AWWA		McDonald Ditto	ea. 8.45
7		8"x1"AWWA		Vega Ditto	ea. 10.00
8		6"x1"AWWA		Dresser Style 91 Double Strap Service Saddle w/1"AWWA tap for A/C pipe 1108	ea. 11.13
9		8"x1"AWWA		Ditto 1147	ea. 15.52
10		10"x1"AWWA		Ditto 1186	ea. 18.51
11		12"x1"AWWA		Ditto 1212	ea. 23.54
12		1" #72		Ford # 72 stainless steel insert stiffner for 1" ips tubing	ea. .37
13				Ametek/Plymouth plastic meter boxes 12" high with 3 1/2" risers and solid plastic lids	ea. 9.50
14		1" #1001		Ford corp stops w/insert	ea. 11.12
15		5/8"x5/4"		Ford V 172 15 coppersettters pack joint in for 1" PE pipe w/1 # 72 insert, pack joint out for 1" PVC, w/SN	ea. 16.04

Prices subject to change without notice

TERMS:

SEE PAGE # 2

SHIPMENT:

TERMS OF WARRANTY:

Goods proving defective in material or workmanship, when used for purposes ordered will be replaced, but no claim for labor or damages will be allowed. All agreements are contingent upon strikes, accidents or other causes beyond our control. Further we strongly urge each contractor to make their own material take-off as we cannot guarantee this material list or the unit quantities as being correct.

WATER WORKS & INDUSTRIAL SUPPLY CO.

By _____

ACCEPTANCE:

We accept the above proposition at the prices shown, subject to any necessary revision in the list of quantities and definite shipping instructions from us.

(CONTRACTOR)

(ADDRESS)

By _____

WATER WORKS & INDUSTRIAL SUPPLY CO.

OFFICE AND WAREHOUSE-2525 GUYAN AVENUE
P. O. BOX 565 TELEPHONE AREA: 304-525-7888
HUNTINGTON, WEST VIRGINIA 25710

BRANCH OFFICES & WAREHOUSES
LEXINGTON, KENTUCKY
606-255-8593

LISTINGS:
WATER WORKS HTG
710-934-8009
WATER WORKS LEX
810-476-8911

PAGE # 2

Date November 8, 1972

TO:

Cox Const. Co.

Date

Project

INQUIRY

Gentlemen:

We wish to submit our QUOTATION on the following list of material, delivery being

Please reference this quotation
number when corresponding on
items shown below.

Shipping Point

F. O. B.

Quotation #

72 141

MAKE OR ITEM	QUAN- TITY	SIZE	CATALOG NO.	DESCRIPTION	UNIT PRICE
16		5/8" x 3/4"		Rockwell SR Cold Water Meter Straight	
				Reading US Gallons less connections	ea. 35.00
17		20"x36"		Sonoco meter wells w/notches	ea. 8.70
18		20"		Ford 20" C 3 meter box covers	ea. 11.18
19				Ford TV172 15 tandem coppersetter	
				both ends pack joint for 1" PE pipe w/2	
				# 72 inserts	ea. 34.91
20		3/4"		Cash E Series 3 pressure regulator	
				300 ADJ 71-100 valve modified per VMS	
				3685 66	ea. 23.42
Items 17 thru 20 are for high pressure settings.					
Prices subject to change without notice					

TERMS: **2% 10 days Net 30 days**

SHIPMENT: **ITEMS 1 thru 18 from stock, items 19 thru 20 2 - 3 weeks after receipt of order.**

TERMS OF WARRANTY: Goods proving defective in material or workmanship, when used for purposes ordered will be replaced, but no claim for labor or damages will be allowed. All agreements are contingent upon strikes, accidents or other causes beyond our control. Further we strongly urge each contractor to make their own material take-off as we cannot guarantee this material list or the unit quantities as being correct.

WATER WORKS & INDUSTRIAL SUPPLY CO.

By *Merrill D. Erwin*

ACCEPTANCE:

Merrill D. Erwin
Executive Vice President

We accept the above proposition at the prices shown, subject to any necessary revision in the list of quantities and definite shipping instructions from us.

(CONTRACTOR)

(ADDRESS)

COX CONSTRUCTION CO.

Bulldozing - Backhoe Service
Concrete Septic Tanks

1815 Galena Pike

W. PORTSMOUTH, OHIO 45662

Phone (614) 858-4400

JOB INVOICE

N^o 3988

BILL TO	Northwest Water System	CUSTOMERS ORDER NO.	92224	DATE ORDERED	2-28-73
ADDRESS	McDermott,	ORDER TAKEN BY		DATE PROMISED	3-6-73
CITY	Ohio	PHONE		DATE ORDERED	2-28-73
		MECHANIC		DATE PROMISED	3-6-73
		HELPER			

JOB NAME AND LOCATION	Donald Breeden McDermott-Pond Ck. Rd.	☐ DAY WORK
DESCRIPTION OF WORK	Water tap installation 8" transite	☐ CONTRACT
	High Pressure	☐ EXTRA

QUANT.	DESCRIPTION OF MATERIAL USED	PRICE	AMOUNT
1	8" Service Saddle Transite		17 07 ^x
1	Corp Stop.		12 23 ^x
1	Tandem Coper Setter		38 40 ^x
1	Kent Meter (Northwest)		no/chg.
1	Sonoco Meter Well		9 57 ^x
1	20" C3 Meter Box Cover		12 30 ^x
1	Cash E Series 3 Pressure Regulator		25 76 ^x
3'	1" pvc 200# test	.10	30 ^x
2'	1" poly pipe 160# test	.23	46 ^x
3'	1/2" resteel - tie wire, gravel		1 50 ^x
2 hrs.	Backhoe - Labor as per contract	19.45	38 90 ^x
Tax Exempt			
HOURS	MECHANICS	AMOUNT	TOTAL MATERIALS
	@		156 49
	HELPERS		TOTAL LABOR
	@		
	TOTAL LABOR		
I hereby acknowledge the satisfactory completion of the above described work:			
SIGNATURE	DATE COMPLETED		TOTAL 156 49

COX CONSTRUCTION CO.

Bulldozing - Backhoe Service

Concrete Septic Tanks

1815 Galena Pike

W. PORTSMOUTH, OHIO 45662

Phone (614) 858-4400

JOB INVOICE

N^o 3773

BILL TO	Northwest Water System	CUSTOMERS ORDER NO.	46-2987-4258	DATE ORDERED	12-15-72
ADDRESS	McDermott	ORDER TAKEN BY		DATE PROMISED	12-15-72
CITY	Ohio	PHONE		DATE ORDERED	12-15-72
		MECHANIC		DATE PROMISED	12-15-72
		HELPER			

JOB NAME AND LOCATION	James Prater Careys Run-Pond Ck. Rd.	☐ DAY WORK
DESCRIPTION OF WORK	Water tap installation 4" tap	☐ CONTRACT
		☐ EXTRA

QUANT.	DESCRIPTION OF MATERIAL USED	PRICE	AMOUNT
1	4" Service Saddle 42 X 1" ANWA		6 88
1	Corp. Stop		12 23
1	Meter Setter		17 64
1	Kent Meter (Northwest)		no/chg
1	Crock - 4 risers - 1 top	10.45	12 20
3'	P.V.C. 200# test	10	30
3'	Poly pipe 160# test	23	69
3'	1/2" resteel, tie wire, bucket stone		1 50
3 1/2 hrs.	Backhoe - labor as per contract	19.45	68 08
Tax exempt			
HOURS	MECHANICS	AMOUNT	TOTAL MATERIALS
	@		119 52
	HELPERS		TOTAL LABOR
	@		10 52
	TOTAL LABOR		109 00
I hereby acknowledge the satisfactory completion of the above described work:			
SIGNATURE	DATE COMPLETED		TOTAL 119 52

COX CONSTRUCTION CO.

JOB INVOICE

Bulldozing - Backhoe Service
Concrete Septic Tanks
1815 Galena Pike
W. PORTSMOUTH, OHIO 45662
Phone (614) 858-4400

NO 4244

CUSTOMER'S ORDER NO. 11252
ORDER TAKEN BY
DATE 4-11-73 (1) A.M. (1) P.M.
4-12-73 (1) P.M.
PHONE

TO: Northwest Water System
FSS McDermott
Ohio

NAME AND LOCATION
Arnold Montgomery Green Valley Estates
DESCRIPTION OF WORK lot -31

ater Tap installation 3" PVC reg. same side

QTY.	DESCRIPTION OF MATERIAL USED	PRICE	AMOUNT
1	3" Service Saddle		6 61 ✓
1	Corp. Stop		12 23 ✓
1	Meter Setter		17 64 ✓
1	Kent Meter (Northwest)		no/chg. ✓
1	Crock - 3 risers - 1 lid		10 45 ✓
1	PVC	.10	30 ✓
1	Poly Pipe	.23	46 ✓
1	½" resteel, tie wire		1 50 ✓
1	½ hrs Backhoe -labor as per contract	19.45	48 63 ✓

MAY 7 1973

tax exempt

LABOR	AMOUNT
MECHANICS @	
HELPERS @	
TOTAL LABOR	97
TOTAL	82 ✓

I hereby acknowledge the satisfactory completion of the above described work.

SIGNATURE

COX CONSTRUCTION CO.

JOB INVOICE

Bulldozing - Backhoe Service
Concrete Septic Tanks
1815 Galena Pike
W. PORTSMOUTH, OHIO 45662
Phone (614) 858-4400

NO 4245

CUSTOMER'S ORDER NO. 11267
ORDER TAKEN BY
DATE 4-4-73 (1) A.M. (1) P.M.
4-12-73 (1) P.M.
PHONE

BILL TO: Northwest Water System
ADDRESS: McDermott
CITY: Ohio

JOB NAME AND LOCATION
Howard - Shaffer Rd. last house on left
DESCRIPTION OF WORK
Water Tap installation 2" PVC reg.

Rd cut - gravel rd

QTY.	DESCRIPTION OF MATERIAL USED	PRICE	AMOUNT
1	2" Service Saddle		5 40 ✓
1	Corp Stop		12 23 ✓
1	Meter Setter		17 64 ✓
1	McKent Meter (Northwest)		no/chg. ✓
1	Crock - 3 risers - 1 lid		10 45 ✓
3	PVC	.10	30 ✓
8	Poly Pipe (total 20')	.23	1 84 ✓
12	Rd. Cut as per contract	2.80	33 60 ✓
2	½" resteel, tie wire		1 50 ✓
	Gravel		3 00 ✓
2 ½	hrs. Backhoe -labor as per contract	19.45	48 63 ✓

MAY 7 1973

LABOR	AMOUNT
MECHANICS @	
HELPERS @	
TOTAL LABOR	131
TOTAL	59

I hereby acknowledge the satisfactory completion of the above described work.

SIGNATURE

COX CONSTRUCTION CO.
Bulldozing - Backhoe Service
Concrete Septic Tanks
1815 Galena Pike
W. PORTSMOUTH, OHIO 45662
Phone (614) 858-4400

JOB INVOICE
NO 4034

COX CONSTRUCTION CO.
Bulldozing - Backhoe Service
Concrete Septic Tanks
1815 Galena Pike
W. PORTSMOUTH, OHIO 45662
Phone (614) 858-4400

JOB INVOICE
NO 4037

CUSTOMER'S ORDER NO.		DATE ORDERED	
11272		4-11-73	
ORDER TAKEN BY		DATE PROMISED	11 A.M.
		5-2-73	11 P.M.
PHONE			
BILL TO Northwest Water System			
ADDRESS McDermott,			
CITY Ohio			
JOB NAME AND LOCATION		11 DAY WORK	
Lloyd Davis - Conloy Rd. off Henley Deemer		11 CONTRACT	
DESCRIPTION OF WORK		11 EXTRA	
Water Tap 2" Reg.			

QTY.	DESCRIPTION OF MATERIAL USED	PRICE	AMOUNT
1	2" Service Saddle		5 40
1	Corp. Stop		12 23
1	Meter Setter		17 64
1	Kent Meter (Northwest)		no/chg.
1	Sonoco Fibre Meter Box 15" & Ford		15 46
2	C-31 Meter Box Cover	.10	20
2	1" PVC	.23	3 22
4	1" Poly pipe		1 50
2	1" Resteel, tiewire		48 63
2-1/2	hrs Backhoe-labor as per contract	19.45	
MAY 7 1973			
HOURS	LABOR	AMOUNT	TOTAL
	MECHANICS @		TOTAL MATERIALS
	HELPERS @		TOTAL LABOR
I hereby acknowledge the satisfactory completion of the above described work.			104 28
SIGNATURE	DATE COMPLETED		TOTAL

CUSTOMER'S ORDER NO.		DATE ORDERED	
11305		4-25-73	
ORDER TAKEN BY		DATE PROMISED	11 A.M.
		5-2-73	11 P.M.
PHONE			
BILL TO Northwest Water System			
ADDRESS McDermott			
CITY Ohio			
JOB NAME AND LOCATION		11 DAY WORK	
Ed Gregory - Heard. off Overville Rd.		11 CONTRACT	
DESCRIPTION OF WORK		11 EXTRA	
Water Tap 10" Transite			

QTY.	DESCRIPTION OF MATERIAL USED	PRICE	AMOUNT
1	10" Service Saddle Transite		21 18
1	Corp Stop		12 23
1	Tandem Copper Setter		38 40
1	Kent Meter (Northwest)		no/chg.
1	Sonoco Meter Well 20"		9 57
1	20" C-3 Meter Box Cover		12 30
1	Cash E. Series 3 Pressure Reg.		25 76
2	1" PVC	.10	20
4	1" Poly pipe	.23	92
2	1/2" resteel, tie wire		1 50
3	hrs. backhoe-labor as per contract	19.45	58 35
MAY 7 1973			
HOURS	LABOR	AMOUNT	TOTAL
	MECHANICS @		TOTAL MATERIALS
	HELPERS @		TOTAL LABOR
I hereby acknowledge the satisfactory completion of the above described work.			100 17
SIGNATURE	DATE COMPLETED		TOTAL

COX CONSTRUCTION CO.

Bulldozing - Backhoe Service
Concrete Septic Tanks
1815 Galena Pike
W. PORTSMOUTH, OHIO 45662
Phone (614) 858-4400

JOB INVOICE
NO 4020

CUSTOMERS ORDER NO.	11301
ORDER TAKEN BY	
DATE ORDERED	4-23-73
DATE PROMISED	4-24-73
PHONE	

BILL TO Northwest Water System

ADDRESS

McDermott,

CITY

Ohio

JOB NAME AND LOCATION

Gerald Piatt - Nauvoo Rd.

DESCRIPTION OF WORK

Water Tap - 4" reg.

☐ DAY WORK☐ CONTRACT☐ EXTRA

MECHANIC

HELPER

QUANT.	DESCRIPTION OF MATERIAL USED	PRICE	AMOUNT
1	4" Service Saddle		6 88✓
1	Corp. Stop		12 23✓
1	Meter Setter		17 64✓
1	Kent Meter (Northwest)		no/chg.
1	Sonoco Fibre Meter Box & 1 Ford C-31 Meter Box cover		15 46✓
3'	PVC pipe	.10	30✓
10'	Poly Pipe	.23	2 30✓
3'	1/2" resteel, tie wire		1 50✓
2-3/4hrs	Backhoe as per contract	19.45	53 49✓

HOURS	MECHANICS	LABOR	AMOUNT	TOTAL MATERIALS
		@		
	HELPERS	@		
I hereby acknowledge the satisfactory completion of the above described work.				TOTAL LABOR
SIGNATURE				TOTAL
				109 80

MAY 7 1973

COX CONSTRUCTION CO.

Bulldozing - Backhoe Service
Concrete Septic Tanks
1815 Galena Pike
W. PORTSMOUTH, OHIO 45662
Phone (614) 858-4400

JOB INVOICE
NO 4019

CUSTOMERS ORDER NO.	11292
ORDER TAKEN BY	
DATE ORDERED	4-17-73
DATE PROMISED	4-20-73
PHONE	

BILL TO Northwest Water System

ADDRESS

McDermott, Ohio

CITY

JOB NAME AND LOCATION

Grady or Ella Spencer - Taylorton Rt.

DESCRIPTION OF WORK

/water tap - 2" PVC Reg.

road cut - oiled

☐ DAY WORK☐ CONTRACT☐ EXTRA

QUANT.	DESCRIPTION OF MATERIAL USED	PRICE	AMOUNT
1	2" Service Saddle		5 94✓
1	Corp. Stop		12 23✓
1	Meter Setter		17 64✓
1	Kent Meter (Northwest)		no/chg.
1	Sonoco Fibre Meter Box 15"		
	1-15" Ford C-31 meter box cover		15 46✓
3'	1" PVC	.10	30✓
20'	1" Poly pipe (total 35' poly)	.23	4 60✓
15'	Rd. Cut as per contract	2.80	42 00✓
2'	1/2" resteel, tie wire		1 50✓
	gravel		3 00✓

3 1/2 hrs.	Backhoe, labor as per contract	19.45	68 08✓
------------	--------------------------------	-------	--------

MAY 7 1973

HOURS	MECHANICS	LABOR	AMOUNT	TOTAL MATERIALS
		@		
	HELPERS	@		
I hereby acknowledge the satisfactory completion of the above described work.				TOTAL LABOR
SIGNATURE				TOTAL
				77 00

COX CONSTRUCTION CO.

Bulldozing - Backhoe Service
Concrete Septic Tanks

1815 Galena Pike
W. PORTSMOUTH, OHIO 45662
Phone (614) 858-4400

Northwest Water System In.
McDermott,
Ohio

Job Name and Location
Rt. 73 - Chid Homes (5)

Description of Work
Repair of replace meter wells

Replaced No. 1-4-5

Repaired No. 2-3 w/parts from 1-4-5

3 Sonoco Fibre Meter Boxes & 3 Ford
C.31 Meter Box covers

4 Hrs. Maintenance crew
labor-small tools-pick-up

9.10 36 40

15.46 46 38

DATE ORDERED
5-7-73

DATE PROMISED
5-23-73

PHONE
MECHANIC
HELPER

DAY WORK
CONTRACT
EXTRA

CUSTOMERS ORDER NO.
11324

ORDER TAKEN BY

DATE ORDERED
5-7-73

DATE PROMISED
5-23-73

PHONE
MECHANIC
HELPER

DAY WORK
CONTRACT
EXTRA

CUSTOMERS ORDER NO.
11324

ORDER TAKEN BY

DATE ORDERED
5-7-73

DATE PROMISED
5-23-73

PHONE
MECHANIC
HELPER

DAY WORK
CONTRACT
EXTRA

CUSTOMERS ORDER NO.
11324

ORDER TAKEN BY

DATE ORDERED
5-7-73

DATE PROMISED
5-23-73

PHONE
MECHANIC
HELPER

DAY WORK
CONTRACT
EXTRA

CUSTOMERS ORDER NO.
11324

ORDER TAKEN BY

COX CONSTRUCTION CO.

Bulldozing - Backhoe Service
Concrete Septic Tanks

1815 Galena Pike
W. PORTSMOUTH, OHIO 45662
Phone (614) 858-4400

Northwest Water System In.
McDermott
Ohio

Job Name and Location
Harry Sherman - Rushtown

Description of Work
Water tap installation 2-3" taps reg.

Replaced No. 1-4-5

Repaired No. 2-3 w/parts from 1-4-5

3 Sonoco Fibre Meter Boxes & 3 Ford
C.31 Meter Box covers

4 Hrs. Maintenance crew
labor-small tools-pick-up

9.10 36 40

15.46 46 38

DATE ORDERED
5-7-73

DATE PROMISED
5-23-73

PHONE
MECHANIC
HELPER

DAY WORK
CONTRACT
EXTRA

CUSTOMERS ORDER NO.
11324

ORDER TAKEN BY

DATE ORDERED
5-7-73

DATE PROMISED
5-23-73

PHONE
MECHANIC
HELPER

DAY WORK
CONTRACT
EXTRA

CUSTOMERS ORDER NO.
11324

ORDER TAKEN BY

DATE ORDERED
5-7-73

DATE PROMISED
5-23-73

PHONE
MECHANIC
HELPER

DAY WORK
CONTRACT
EXTRA

CUSTOMERS ORDER NO.
11324

ORDER TAKEN BY

DATE ORDERED
5-7-73

DATE PROMISED
5-23-73

PHONE
MECHANIC
HELPER

DAY WORK
CONTRACT
EXTRA

CUSTOMERS ORDER NO.
11324

ORDER TAKEN BY

COX CONSTRUCTION CO.

Bulldozing - Backhoe Service
Concrete Septic Tanks

1815 Galena Pike
W. PORTSMOUTH, OHIO 45662
Phone (614) 858-4400

Northwest Water System In.
McDermott
Ohio

Job Name and Location
Harry Sherman - Rushtown

Description of Work
Water tap installation 2-3" taps reg.

Replaced No. 1-4-5

Repaired No. 2-3 w/parts from 1-4-5

3 Sonoco Fibre Meter Boxes & 3 Ford
C.31 Meter Box covers

4 Hrs. Maintenance crew
labor-small tools-pick-up

9.10 36 40

15.46 46 38

DATE ORDERED
5-7-73

DATE PROMISED
5-23-73

PHONE
MECHANIC
HELPER

DAY WORK
CONTRACT
EXTRA

CUSTOMERS ORDER NO.
11324

ORDER TAKEN BY

DATE ORDERED
5-7-73

DATE PROMISED
5-23-73

PHONE
MECHANIC
HELPER

DAY WORK
CONTRACT
EXTRA

CUSTOMERS ORDER NO.
11324

ORDER TAKEN BY

DATE ORDERED
5-7-73

DATE PROMISED
5-23-73

PHONE
MECHANIC
HELPER

DAY WORK
CONTRACT
EXTRA

CUSTOMERS ORDER NO.
11324

ORDER TAKEN BY

DATE ORDERED
5-7-73

DATE PROMISED
5-23-73

PHONE
MECHANIC
HELPER

DAY WORK
CONTRACT
EXTRA

CUSTOMERS ORDER NO.
11324

ORDER TAKEN BY

JOB INVOICE

No. 5581

Northwest Water System Inc.

P. O. Box 5

city

PROVERBIAL, ONTO
JOB NAME AND LOCATION

Community Human & Industrial Development
DESCRIPTION OF ACTIVITY:

McDermott/Pond Uk. Rd.

Water Tap installation 7 taps 2" PVC reg

Rd. Bore			
QUANT.	DESCRIPTION OF MATERIAL USED	PRICE	AMOUNT
7	2" Service Saddles	5.94	41.58
7	Corp. Stop	12.23	85.61
7	Meter Setter	17.64	123.48
7	Kent Meter xx(Northwest)		no/chg.
7	Sonoco Fibre Meter Box & Ford		
	C-31 Meter Box covers	15.46	108.22
14'	PVC 1"	.10	1.40
28'	1" Poly	.23	6.44
14'	1/2" resteel tie wire.		10.50
1	8"x2" Baker 195 Service Saddle		20.98
2	2" Brass nipples	2.44	4.88
1	2" Hammond 609 Gate Valve		23.56
1	2" PVC Adapter MAF200S		2.93
3	2" 90° Elbows	1.00	3.00
1	2" Cap		68
536	2" PVC pipe (total 555')	3.29	155.44
19'	Road Bore as per contract 2" line	3.50	66.50
26 hrs.	Backhoe labor as per contract	19.45	505.70
	MECHANICS @	TOTAL MATERIALS	
	HELPERS @	TOTAL LABOR	
I hereby acknowledge the satisfactory completion of the above described work:		TOTAL	1160.90
SIGNATURE		DATE COMPLETED	

COX CONSTRUCTION CO.
Bulldozing - Backhoe Service
Concrete Septic Tanks

JOB INVOICE
No 5569

JOB INVOICE
No 5567

1815 Galena Pike
W. PORTSMOUTH, OHIO 45662
Phone 614 858-4400

CUSTOMERS ORDER NO.	DATE ORDERED
11485	12-11-73
ORDER TAKEN BY	DATE PROMISED
	12-21-73
	5 A.M. P.M.
	PHONE

1815 Galena Pike
W. PORTSMOUTH, OHIO 45662
Phone 614 858-4400

LL TO
Northwest Water Inc.

LL TO		T.C. - C.L. - / P.M.
<u>ADDRESS</u>	Northwest Water Inc.	PHONE
	Box 5	MECHANIC
<u>Y</u>		HELPER

BILL TO	Northwest Water System Inc.		
ADDRESS	Box 5		
CITY	M.D.		
PHONE	1-2-20-11	11 P.M.	
MECHANIC			
HELPER			

DOB	NAME AND LOCATION	Worstel Address
	McDermott, Ohio	
	Dale Harris	

McDermott, Ohio		☐ DAY WORK
JB NAME AND LOCATION		☐ CONTRACT
Dale Harris	Worstel Add	☐ EXTRA
DESCRIPTION OF WORK		
Water tap installation		

JOB NAME AND LOCATION McDermott, Ohio	☐ DAY WORK ☐ CONTRACT ☐ EXTRA
DESCRIPTION OF WORK Ralph Bradshaw Water Tap installation	

3" line reg. tap

3" line res. tap

1" line reg tap

[illegible][illegible]
